

What's Happening:

The interior of the building is moving quickly to take shape. Masonry walls are going up, steel studs are being erected, and in wall MEPs are being installed. Moving west to east the steel framing has approached rough completion with the electrician and plumber close behind. On the exterior of the building, IMP panels getting finished up and the installers will move onto the metal panel covering the rest of the building. The site has changed a lot as well. Site prep was completed early this week to open the site up for curb and gutter to be installed around the building. The retention ponds are also starting to resemble the finished product.


Coming very soon we will see a lot of progress on the entire site. Concrete will continue to be poured around the exterior with sidewalks coming after the curb and gutter. After the masonry walls finish inside the building, the masons will move back outside to finish up the brick and stone veneer on the outside. Framing and MEPs will continue to install with the framers transitioning to drywall in the next few weeks.



The curb and gutter has been poured around the site, outlining the parking lot and sidewalks.



Insulated metal panel has moved past the north side of the building, moving closer to completion.

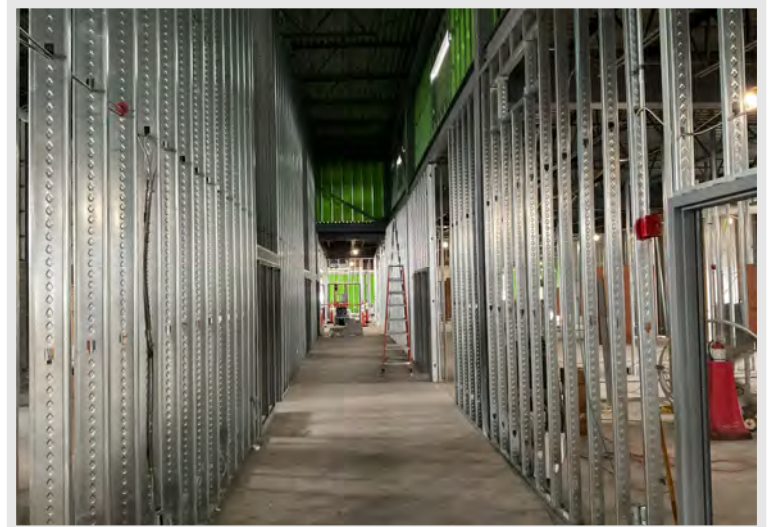

The interior is taking shape as framing sections out the different rooms.

DID YOU KNOW?

Did you know, unlike most other ways concrete is used, curb and gutter are poured without any forms. A curb and gutter machine, also known as a power curber, drives the course of the curb and uses an attached form to mold the concrete into shape. Curbs are poured with a lot stiffer concrete which allows it to hold its shape after the machine moves on.

Questions?

Project Manager, Matt McDonald / (608)-301-6169 / mmcdonald@findorff.com



The air vapor barrier has been completed and the exterior sheathing is all sealed



The site workers are placing the rock around the retention ponds



The retaining ponds are already holding water after all the rain we got this week.

Questions?

Project Manager, Matt McDonald / (608)-301-6169 / mmcdonald@findorff.com
